



## Construction Update - July 16, 2022

This week, the contractor excavated and placed the subbase behind the cofferdam. This work is done in preparation for the retaining wall installation on both the south side of Crystal Creek and west side of Main Street. AT&T was also on-site splicing cable for new infrastructure near 111 S. Jefferson Street.

Next week, crews plan to continue excavation work and placing additional subbase. Weather permitting, the crews also plan to pour concrete footings needed for the retaining wall installation.



*Subbase Placement*



# WHAT ARE *Cofferdams*?

**cof·fer·dam**

/ˈkɒfər,dam


a watertight enclosure pumped dry to permit construction work below the waterline, as when building bridges



COFFERDAMS CREATE DRY CONSTRUCTION WORK AREAS



COFFERDAM BUILT AT MAIN STREET

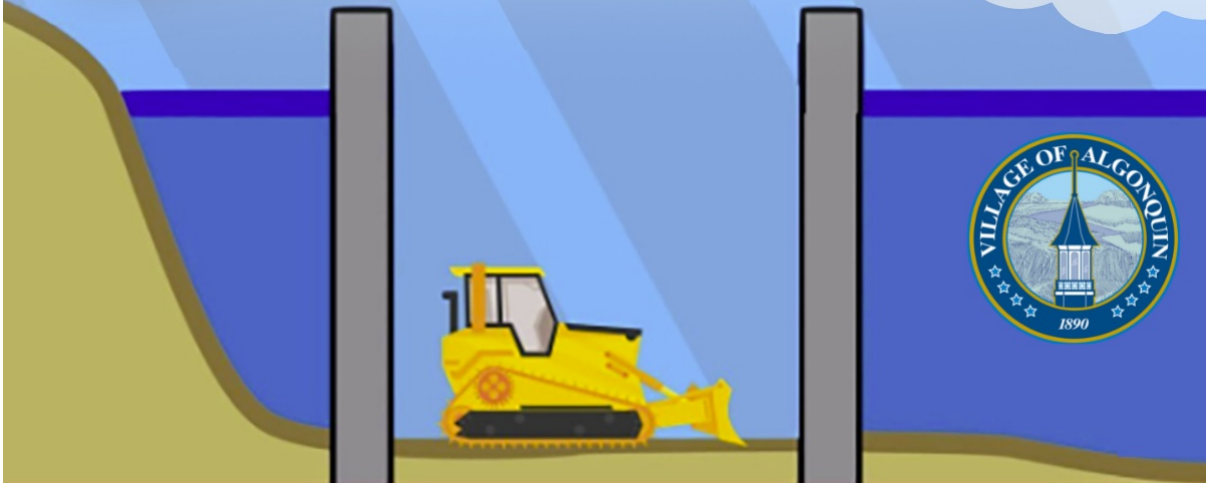

## Stage 1

WINTER 2021 - SUMMER 2022

Harrison Street Bridge Reconstruction  
Riverwalk Construction & Parking  
Crystal Creek Improvements  
Historic Village Hall Parking Lot Reconstruction

## Stage 2

SPRING 2022 - FALL 2022

20 W. Washington Street Parking Lot Construction

## Stage 3

SPRING 2023 - FALL/WINTER 2023

Washington Street Streetscape  
Harrison Street Streetscape  
Harrison Street Utility Undergrounding  
Downtown Streets Resurfacing

## Stage 4

FALL 2023 - SPRING 2024

Village Parking Lot Resurfacing

## Stage 5

FALL 2023 - SPRING 2024

Downtown Parking Concept Plan



Sign up for  
Email Updates

