



## Construction Update - July 2, 2022

This week, the contractor performed excavation behind the cofferdam in preparation for the retaining wall installation on the south side of Crystal Creek, west of Main Street.

Over the next two weeks, excavation and retaining wall installation will be ongoing.

Utility companies will also continue working to transfer existing customers to the new infrastructure on S. Harrison Street.



*Cofferdam in Crystal Creek*



# WHAT ARE *Cofferdams*?

**cof·fer·dam**

*/ˈkɒfər,dam*


a watertight enclosure pumped dry to permit construction work below the waterline, as when building bridges



COFFERDAMS CREATE DRY  
CONSTRUCTION WORK AREAS



COFFERDAM BUILT AT  
MAIN STREET

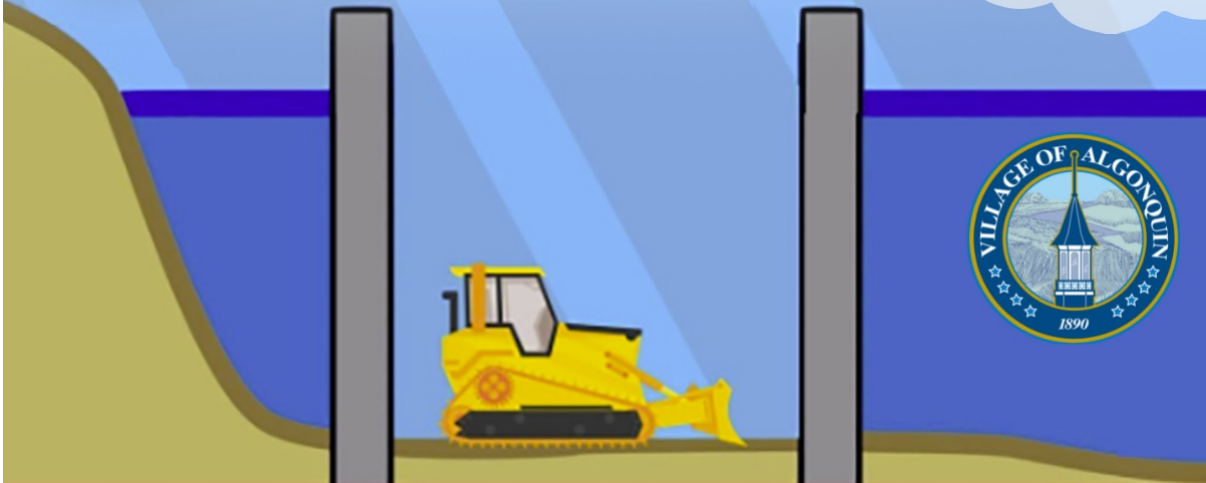

## Stage 1

WINTER 2021 - SUMMER 2022

Harrison Street Bridge Reconstruction  
Riverwalk Construction & Parking  
Crystal Creek Improvements  
Historic Village Hall Parking Lot Reconstruction

## Stage 2

SPRING 2022 - FALL 2022

20 W. Washington Street Parking Lot Construction

## Stage 3

SPRING 2023 - FALL/WINTER 2023

Washington Street Streetscape  
Harrison Street Streetscape  
Harrison Street Utility Undergrounding  
Downtown Streets Resurfacing

## Stage 4

FALL 2023 - SPRING 2024

Village Parking Lot Resurfacing

## Stage 5

FALL 2023 - SPRING 2024

Downtown Parking Concept Plan



Sign up for  
Email Updates

