



Construction Update - May 28, 2022

For the past two weeks, Comcast and AT&T have been working to pull and install new service pedestals on the west side of Main Street. The construction crew also completed the extension of the existing 6" water main at 111 S. Jefferson Street.

Over the next few weeks, crews will install new water services for 111 S. Jefferson Street and 100 S. Main Street. The contractor will then begin driving sheeting at Crystal Creek to build a cofferdam on the west side of Main Street. Cofferdams create a watertight enclosure which allows construction within Crystal Creek.


The utility companies will also transfer all existing costumers on the west side of Main Street to the newly installed service infrastructure and install new cable and pedestals on S. Harrison Street.



Comcast and AT&T Cable Work



AT&T Cable Work

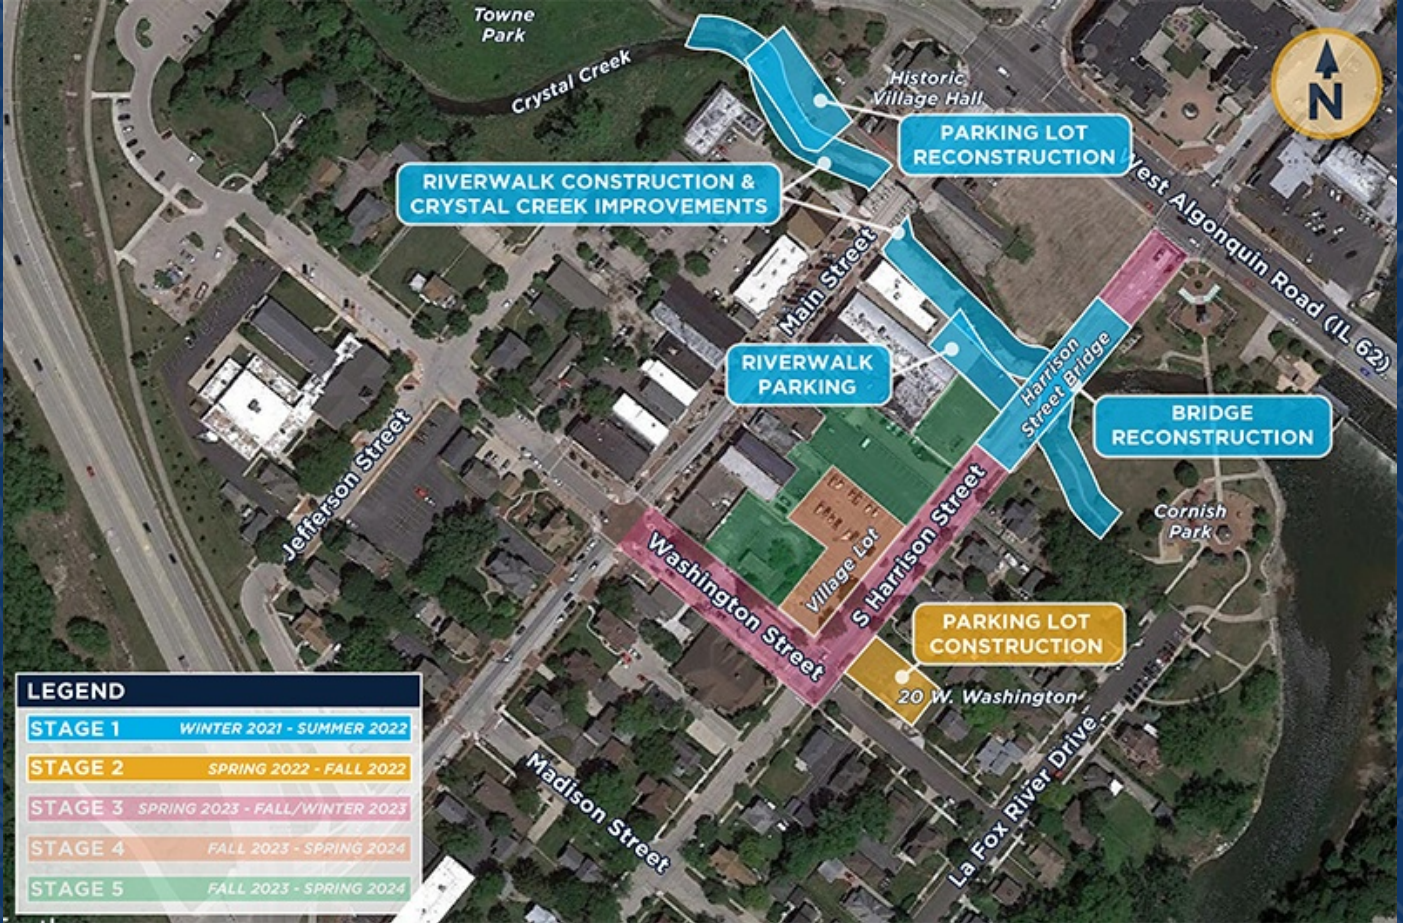

Stage 1

WINTER 2021 - SUMMER 2022

Harrison Street Bridge Reconstruction
 Riverwalk Construction & Parking
 Crystal Creek Improvements
 Historic Village Hall Parking Lot Reconstruction

Stage 2

SPRING 2022 - FALL 2022

20 W. Washington Street Parking Lot Construction

Stage 3

SPRING 2023 - FALL/WINTER 2023

Washington Street Streetscape
 Harrison Street Streetscape
 Harrison Street Utility Undergrounding
 Downtown Streets Resurfacing

Stage 4

FALL 2023 - SPRING 2024

Village Parking Lot Resurfacing

Stage 5

FALL 2023 - SPRING 2024

Downtown Parking Concept Plan



Sign up for
Email Updates



